Memorandum



DATE January 13, 2011

To Trinity River Corridor Project Committee Members:

David A. Neumann (Chairman) Vonciel Jones Hill

Steve Salazar (Vice-Chair)

Mayor Pro Tem Dwaine Caraway

Delia Jasso

Linda Koop

Deputy Mayor Pro Tem Pauline Medrano

Ann Margolin

Carolyn R. Davis

SUBJECT Standing Wave and Santa Fe Trestle Trail

The attached briefing on the Standing Wave and Santa Fe Trestle Trail will be presented at the January 18, 2011 Trinity River Corridor Project Committee Meeting. The briefing will provide a schedule and progress report, including photographs of the work done to date.

Please contact me if you have questions.

Jill A. Jordan, P.E. Assistant City Manager

THE TRINITY

.....

Attachment

C: Honorable Mayor and Members of the City Council Mary K. Suhm, City Manager Ryan S. Evans, First Assistant City Manager A.C. Gonzalez, Assistant City Manager Forest E. Turner, Assistant City Manager Jeanne Chipperfield, Chief Financial Officer Deborah A. Watkins, City Secretary Thomas P. Perkins, Jr., City Attorney Craig D. Kinton, City Auditor Judge C. Victor Lander Helena Stevens-Thompson, Asst. to the City Manager Frank Librio, Director, Public Information Office Kelly High, Director, Trinity Watershed Management Rebecca Rasor, P.E., Managing Director, Trinity River Corridor Project



THE TRINITY DALLAS

Standing Wave and Santa Fe Trestle Trail



Trinity River Corridor Project Committee


January 18, 2011





Standing Wave



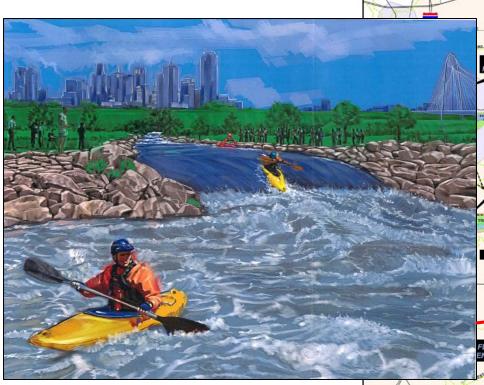

Santa Fe Trestle Trail

Proposed Lakes

Trinity River

Levees

Proposed Chain of Wetlands

Elm Fork Area Flood Protection Study

/ Canyon/Mixmaster

Dallas County

Dallas City Limits

Whitewater Course

 ✓ Proposed Toll Road Possible Trinity River Interpretive Center Sites **Proposed Soccer Complex** Existing Lakes

✓ Proposed Trinity Trails

Other Parks and Greenbelts


Trinity River Corridor Parks

Possible Trinity River Equestrian Center Sites

Possible Trinity River Gateway Parks

Boat Launches
Completed Launches
Launches Under Design



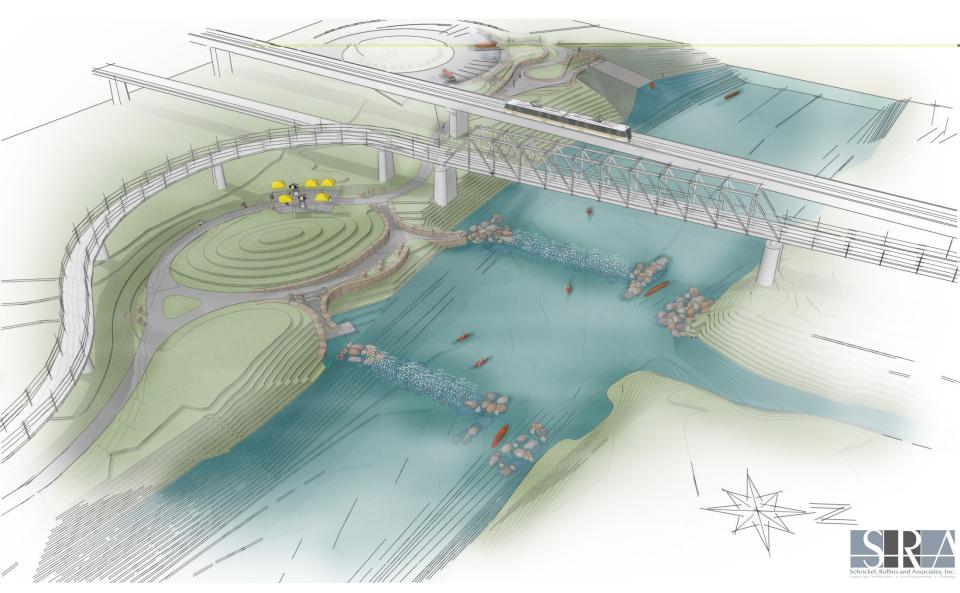



Standing Wave

- \$200,000 from the 1998 Bond Program
- \$3.2 million from the 2006 Bond Program
- Contract awarded November 2009
- Santa Fe Trestle Trail
 - \$2 million from the 1998 Bond Program
 - Additional \$3.5 million from Statewide Transportation Enhancement Program (STEP) grant, TxDOT
 - Contract awarded May 2010






Contractor built a cofferdam and diverted the river channel to be able to work in a dry area





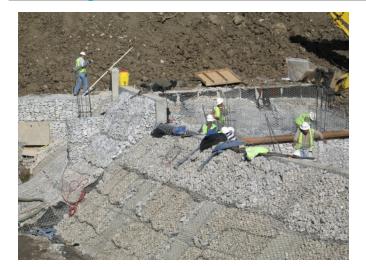



 On December 22, 2010, Ark Construction began removing the cofferdam around the Standing Wave Construction



 Representative from REP (design subcontractor) entered the whitewater to check wave function and safety












Photos taken January 7, 2011



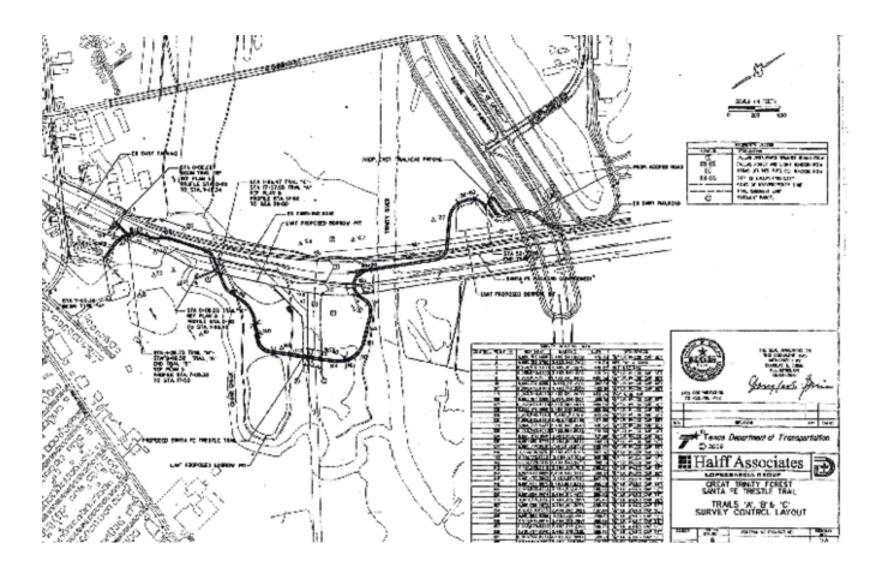






Parking lot construction on east overbank



Raised trail allows some floodwaters to pass



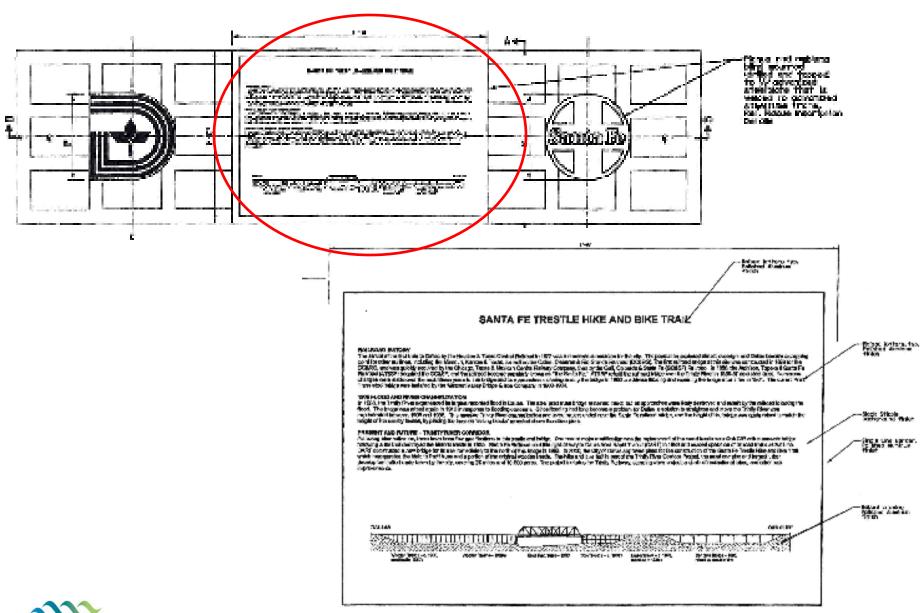



- Standing Wave is expected to be complete in Spring 2011
- Santa Fe Trestle Trail is expected to be complete in Fall 2011
- Both construction schedules are weather dependent



Trinity River Project Office (214) 671-9500

www.trinityrivercorridor.org ftp://ftp.dallascityhall.com



